



WEEKLY SUMMARY
EAU CLAIRE SCHOOLS
PUTNAM HEIGHTS
ELEMENTARY

SCHEDULE UPDATE

Current Week:

- Market & Johnson continued with supervision and coordination.
- M&J-Finished floor prep.
- M&J- Poured and finished remaining floors.
- Hudson Elec- Above ceiling conduit in multiple areas.
- M&J-Laid out metal stud walls and CMU walls.

Upcoming Week:

- Market & Johnson- Continue with supervision and coordination.
- M&J- Framing material delivery.
- Badger State- Bathroom A109 & A109A rough in.
- M&J- Metal stud wall framing.
- Ryan Jack Painting- Acoustical caulking at corridor CMU walls.
- Hudson Elec- Continue above ceiling and in wall rough in's.
- Winona Controls- HVAC Rough in's.

WEEKLY PHOTOS




Art Room/Smart Room A112 & A118





Center corridor A102

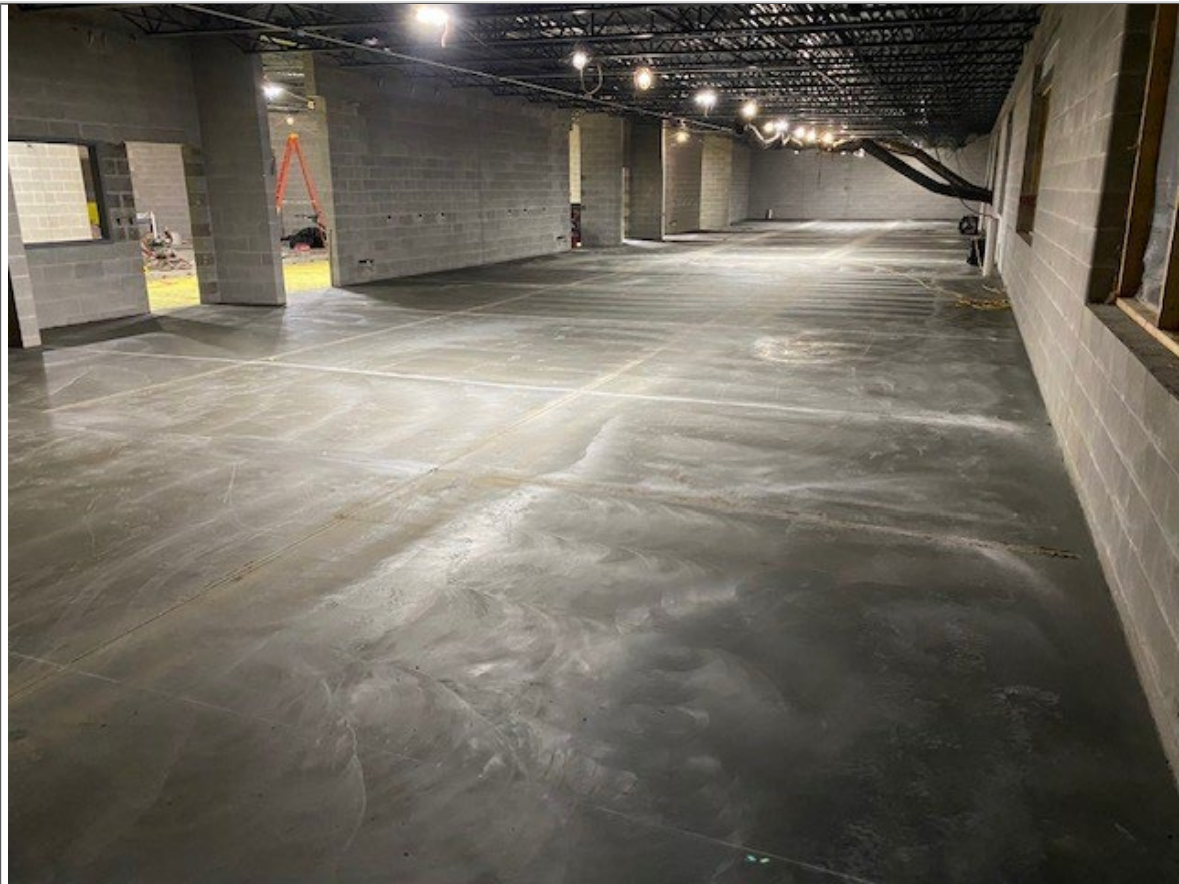

East side classrooms 132-120
