



*Adding Value to Everything We Do*

WEEKLY SUMMARY

EAU CLAIRE SCHOOLS  
NORTH HIGH SCHOOL

## SCHEDULE UPDATE

### Current Week:


- Market & Johnson masons completed brick veneer and disassembled shelter and scaffold to be trucked off site.
- Market and Johnson carpenters continued with setting interior window and door frames, wall framing and installing wood backing.
- Hudson Electric continued with boxes and conduit for electrical rough in.
- NL Stock completed rough in of PVC drain and vent piping.
- Master Mechanical installed overhead hangers for new HVAC duct and piping.


### Upcoming Week:

- Market & Johnson will continue with wall framing and wood backing along with beginning to hang drywall and insulate walls with sound batts.
- Hudson Electric and Master Mechanical will continue with electrical and HVAC rough ins.

## WEEKLY PHOTOS



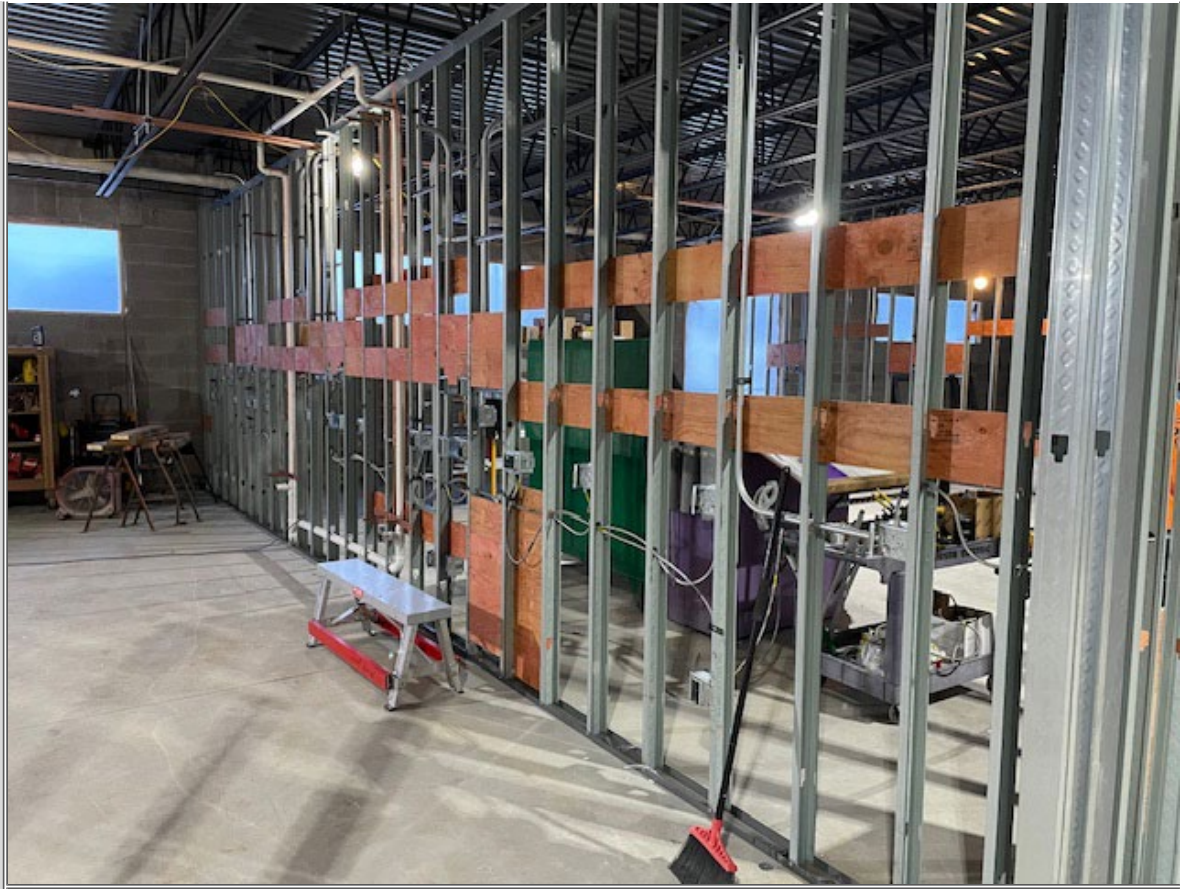

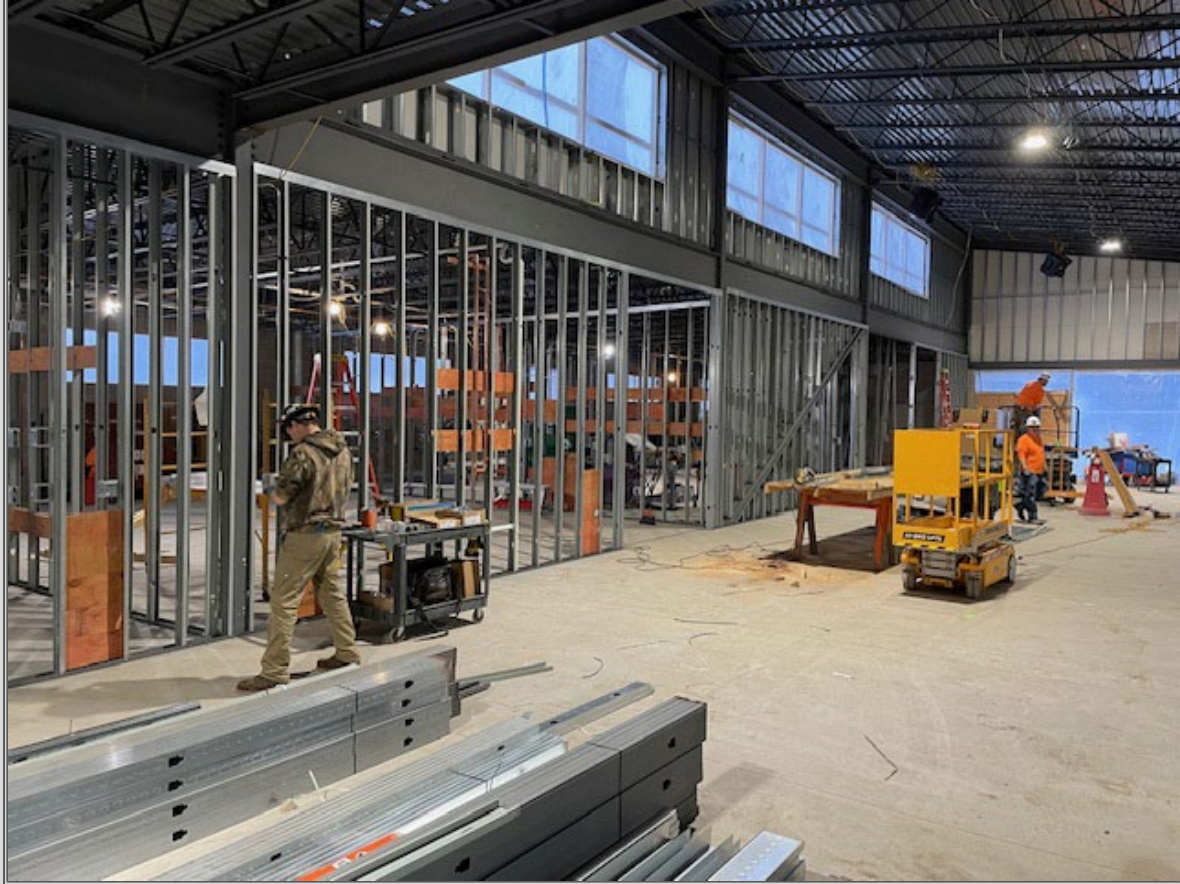



**PPE REQUIRED**

**ON THIS SITE AT ALL TIMES**

- HARD HATS
- SAFETY GLASSES
- HI-VIS CLOTHING



My Market Johnson
