



WEEKLY SUMMARY

EAU CLAIRE SCHOOLS NORTH HIGH SCHOOL

SCHEDULE UPDATE

Current Week:


- Market & Johnson continued with metal framing, HM frame installation, wood backing, drywalling along with acoustical caulking and sound batts.
- NL Stock continued with plumbing supply line rough ins.
- Hudson Electric continued with electrical rough ins.
- Master Mechanical continued to install piping and ductwork for HVAC at new addition.

Upcoming Week:

- Market & Johnson will continue with drywall and sound batts as well as install shoring for sawing of new openings in existing masonry walls.
- Hudson Electric, NL Stock and Master Mechanical will continue with rough ins.
- Cutting Edge will saw openings in existing masonry walls for new corridor and a new window opening.

WEEKLY PHOTOS



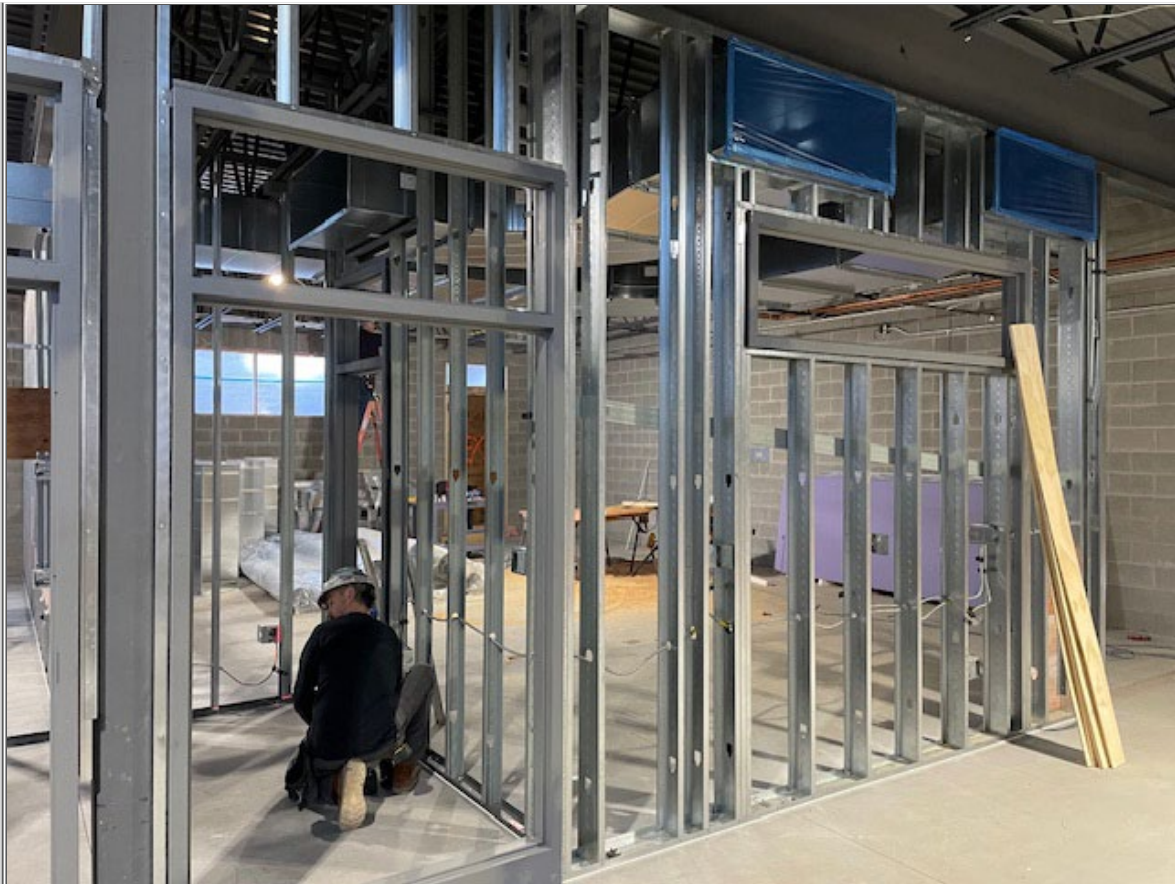



N.L. Sto
PL

