



## WEEKLY SUMMARY

# EAU CLAIRE SCHOOLS SOUTH MIDDLE SCHOOL

### SCHEDULE UPDATE

#### Current Week:

- Market & Johnson continued with supervision and coordination. M&J poured concrete floor slabs in area A and B additions both floors. Started interior stud framing. Masons started exterior brick on area A addition.
- D7 finished air barrier on area D addition.
- RTS roofing was off site.
- Winona Controls contained plumbing rough-in on area B science labs.


#### Upcoming Week:

- Market & Johnson will continue with supervision and coordination. Continue interior steel stud framing. Pour concrete slab in front entrance addition. Masons will continue exterior brick on area A addition.
- RTS roofing will finish roof on front entrance addition.
- Winona Controls will continue plumbing rough-in.
- Master Metals will start installing HVAC in area B addition.
- B&B electric will start electrical rough-in.

### WEEKLY PHOTOS



Floors poured area B, started framing walls

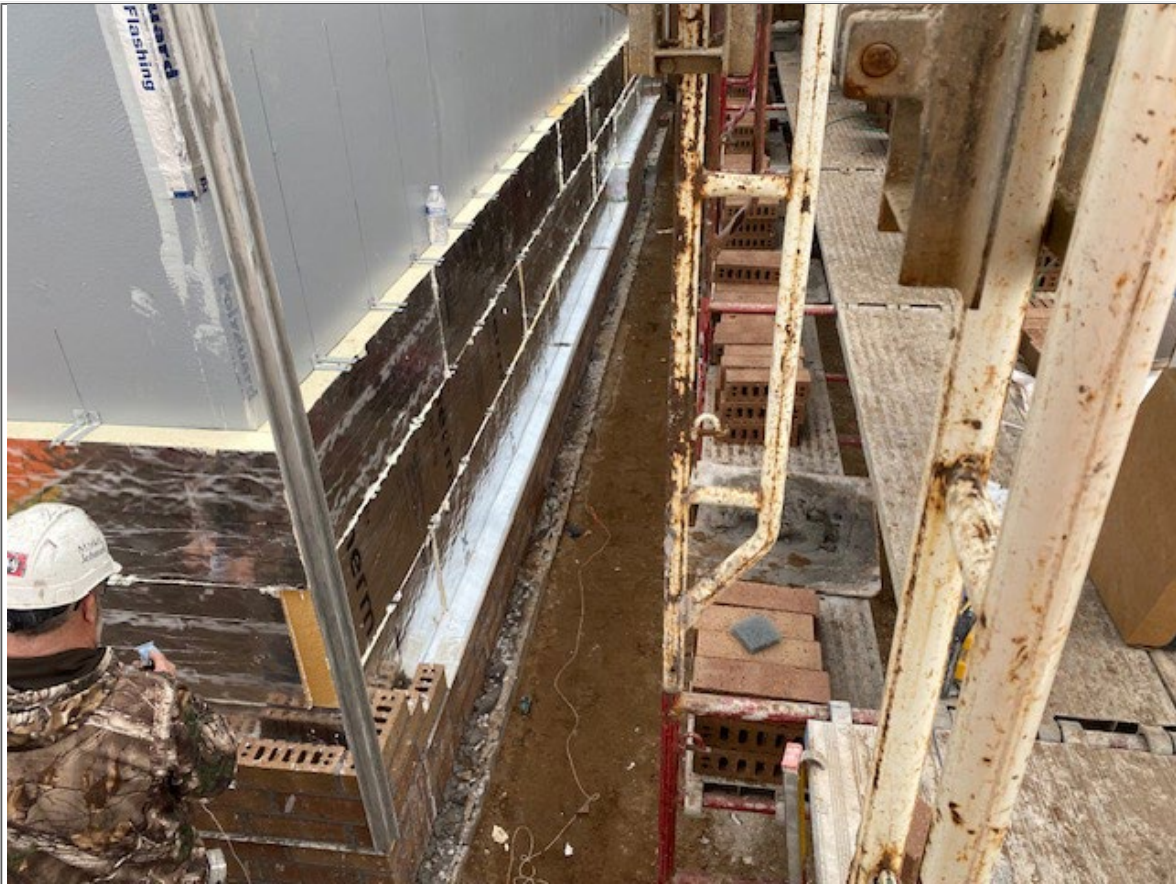

Brick area A





Scaffold for brick area A

