

SCHEDULE UPDATE

Current Week:

- Market & Johnson continued with supervision and coordination. M&J continued interior stud framing and backing. Masons continued exterior brick on area B & D additions.
- B&B, Master Metals, and Winona Controls continued area B and D MEP rough-ins.


Upcoming Week:

- Market & Johnson will continue with supervision and coordination. Continue area A interior steel stud framing and begin hanging drywall. Masons will complete exterior brick at area A, B, and D additions. M&J will begin removing corridor ceiling tiles and infilling windows connected to the additions.
- Winona Controls will continue plumbing rough-in.
- Master Metals will continue HVAC installation.
- B&B electric will continue electrical rough-in.

WEEKLY PHOTOS



Area D Addition

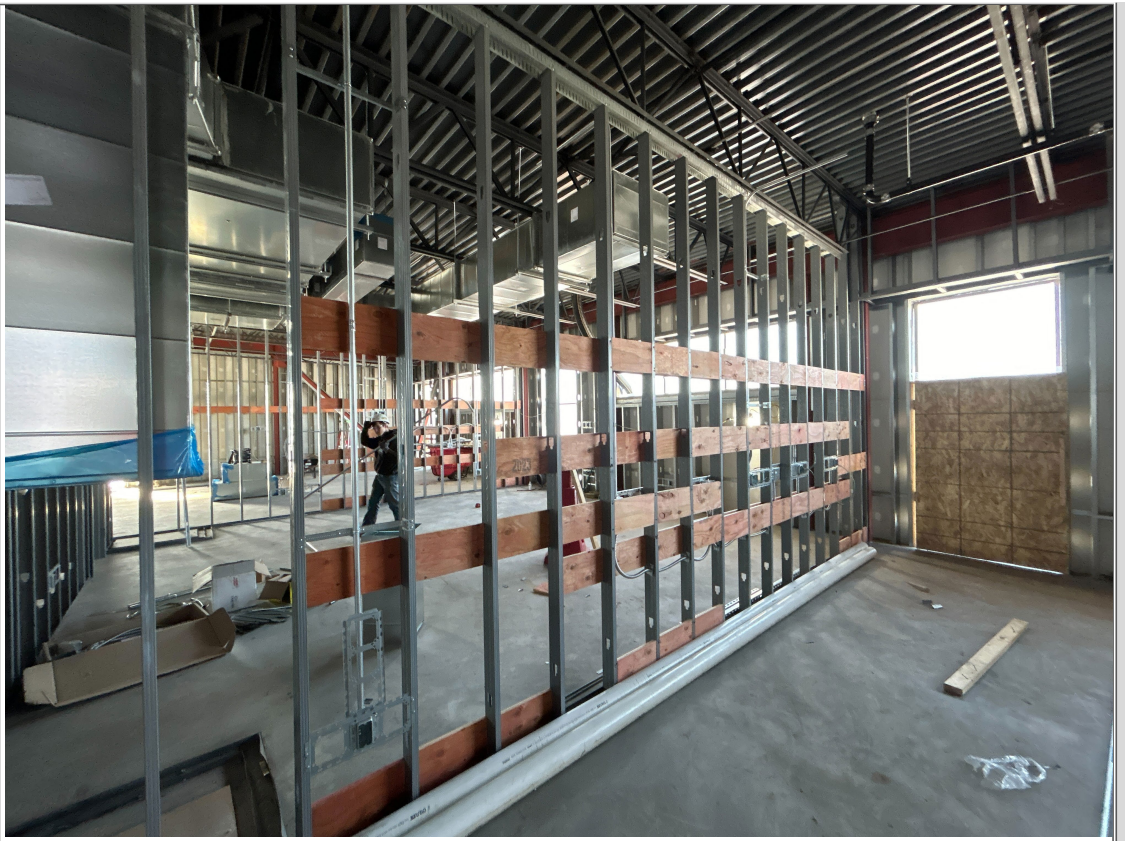

Area B Addition, 2nd Floor



