



## WEEKLY SUMMARY

# EAU CLAIRE SCHOOLS NORTH HIGH SCHOOL

### SCHEDULE UPDATE

#### Current Week:

- Market & Johnson continued installing door hardware, markerboards, tackboards, and began building soffits in rooms 233, 235, and 239.
- Badger Washing cleaned the exterior brick.
- Esser Glass continued installing glass at interior HM frames and at the Vestibule Storefront.
- Hudson Electric continued installing devices and lighting.
- Ryan Jack Painting continued with priming and painting the Clearstory walls.
- PCI Austad continued installing ceiling grid in new classrooms.

#### Upcoming Week:

- Market & Johnson will continue installing door hardware, markerboards, tackboards, and building soffits.
- Hudson Electric will continue installing devices and lights.
- Ryan Jack Painting will begin taping, priming, and painting walls in rooms 233, 235, and 239.
- PCI Austad will continue installing ceiling grid and begin hanging fabric panels in the Clearstory.
- Esser Glass will begin installing break metal and interior/exterior caulking.
- MLS Enterprises, LLC. will begin installing metal panels on the Clearstory exterior.
- Swanson's Flooring will begin installing LVT flooring in the new classrooms.


### WEEKLY PHOTOS



Clearstory Commons



Room 233

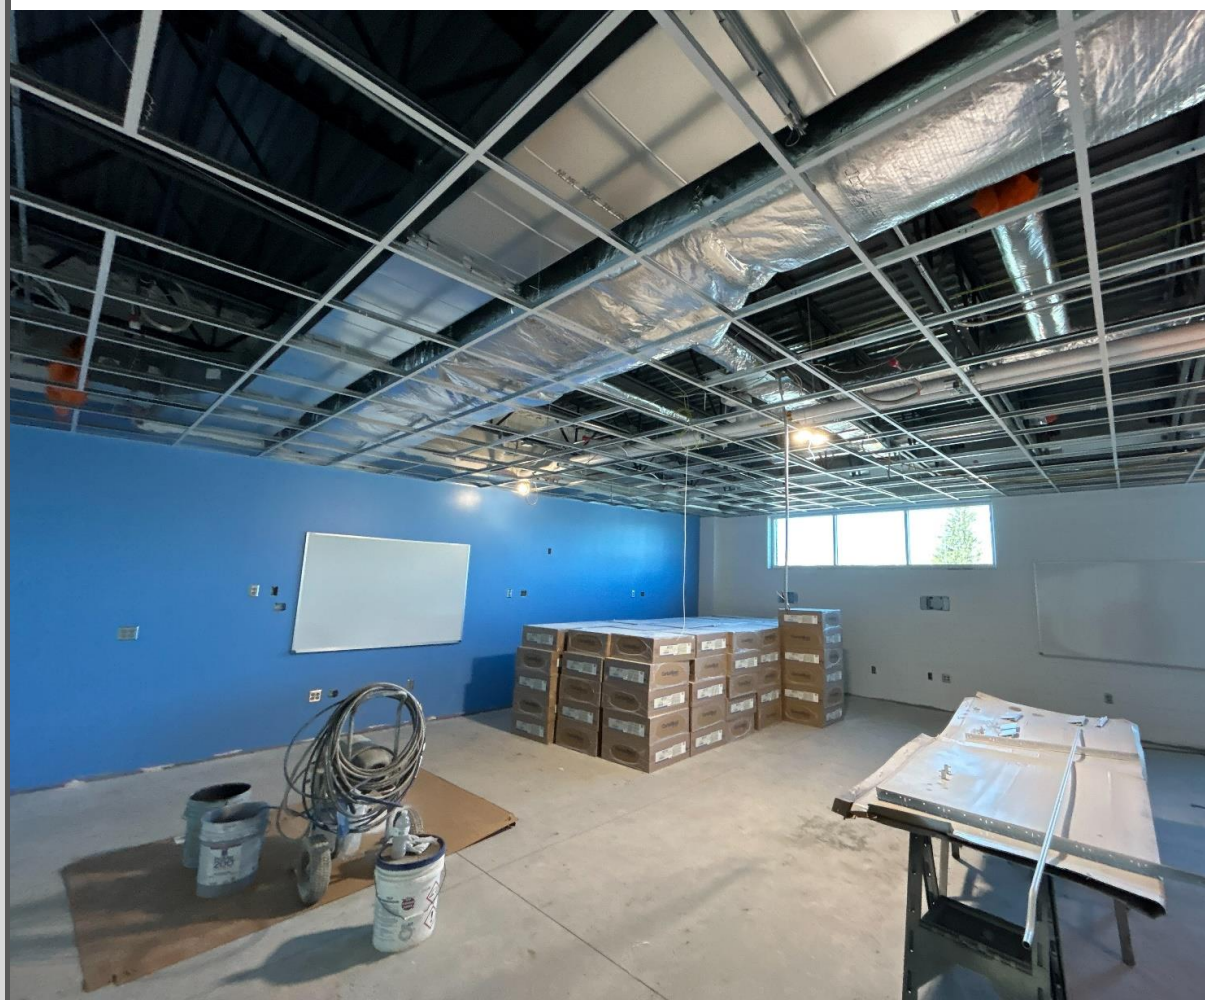

Ceiling Grid Installed





Installing Marker Boards

**Have Questions? Contact:**

Project Manager

Jordan Lieftring

715-579-0176

[jlieftring@market-johnson.com](mailto:jlieftring@market-johnson.com)

Superintendent

Jeremy Hollister

715-579-7991

[jhollister@market-johnson.com](mailto:jhollister@market-johnson.com)
