



EAU CLAIRE
AREA SCHOOL DISTRICT



CAPITAL REFERENDUM 2022 PROJECT UPDATES

June 19, 2023

MANZ ELEMENTARY BOILER AND PUMP REPLACEMENT: The demolition is complete, and the boiler is set in place. The contractor has begun reworking the piping and making the final connections to the new boiler. Xcel Energy installed a new gas meter which was relocated to comply with new code requirements. The boiler project should be completed by mid-July.



SHERMAN ELEMENTARY GYM WALL DIVIDER REPLACEMENT: The demolition of the existing wall divider is complete. The new track, motor and control switches are installed. The divider door is on order and is estimated to arrive the second week in August. The contractor will come at that time to install the new divider door.

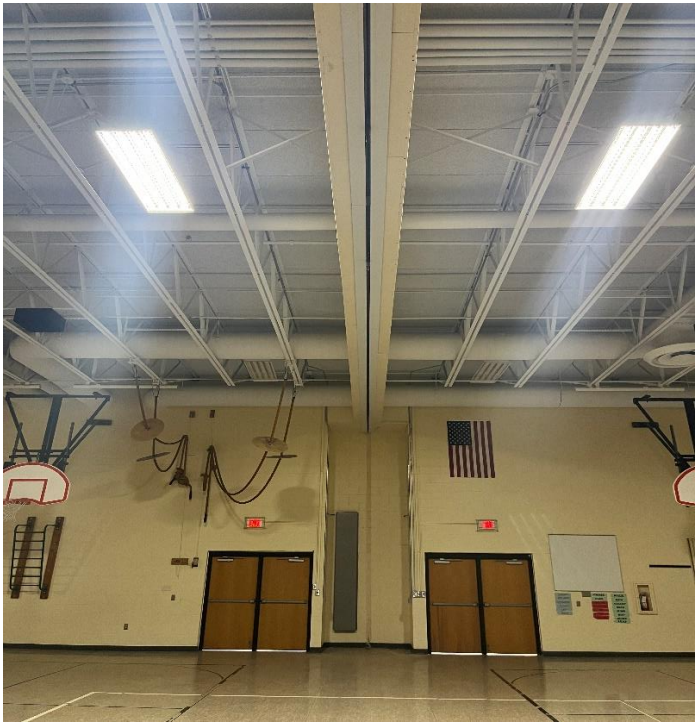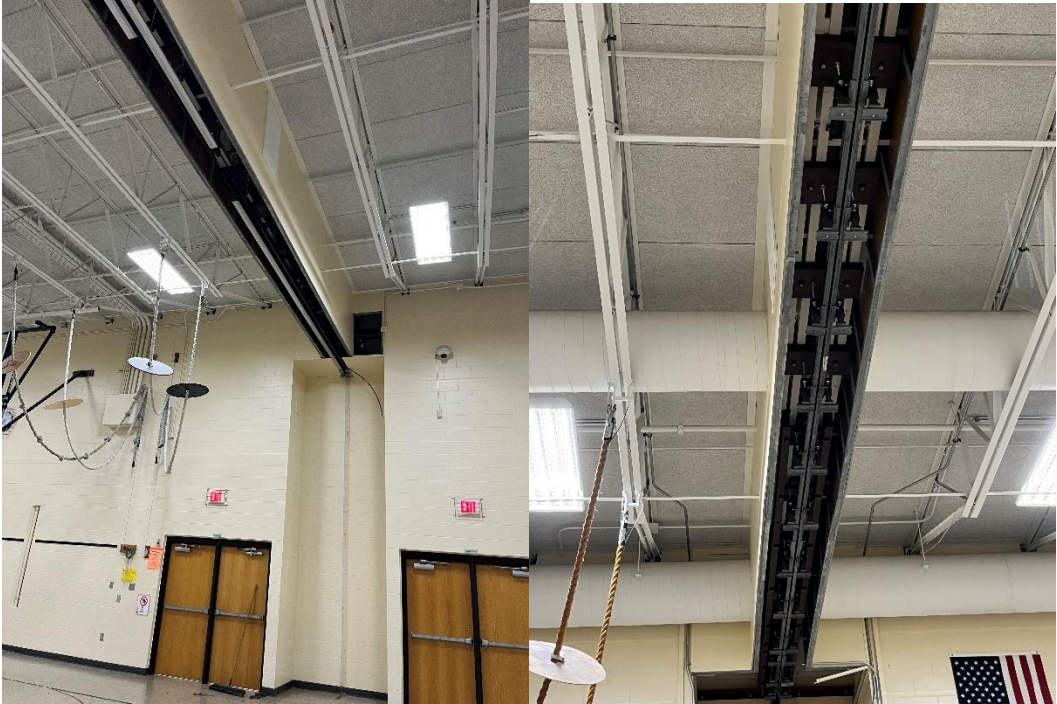

NORTH HIGH FLOORING REPLACEMENT

The work will begin the week of June 19.

MEMORIAL HIGH FLOORING REPLACEMENT

The work will begin the week of July 10.

LOCUST LANE ELEMENTARY AIR HANDLING UNIT AND VARIABLE AIR VOLUME REPLACEMENT

The project is currently out for bid. Bid opening will be on June 22.

NORTHWOODS ELEMENTARY AIR HANDLING UNIT AND BOILER REPLACEMENT

The project is currently out for bid. Bid opening will be on June 22.

MEADOWVIEW ELEMENTARY BOILER REPLACEMENT

The project is currently out for bid. Bid opening will be on June 22.

NORTHSTAR MIDDLE POOL AIR HANDLING UNIT REPLACEMENT

The project is currently out for bid. Bid opening will be on June 22.
